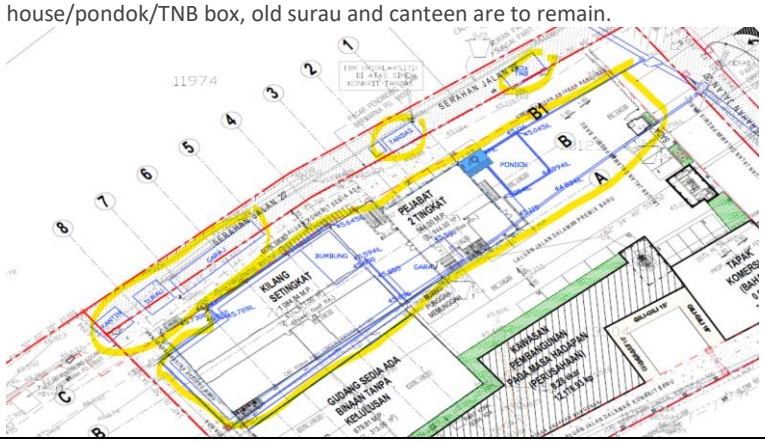
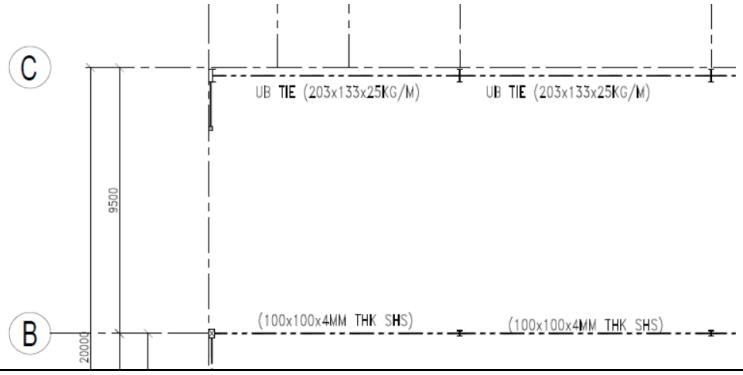
AB MALAYA SDN BHD
(1601411-W)

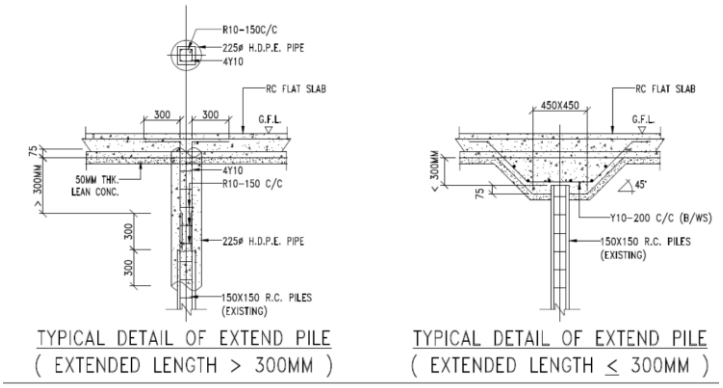
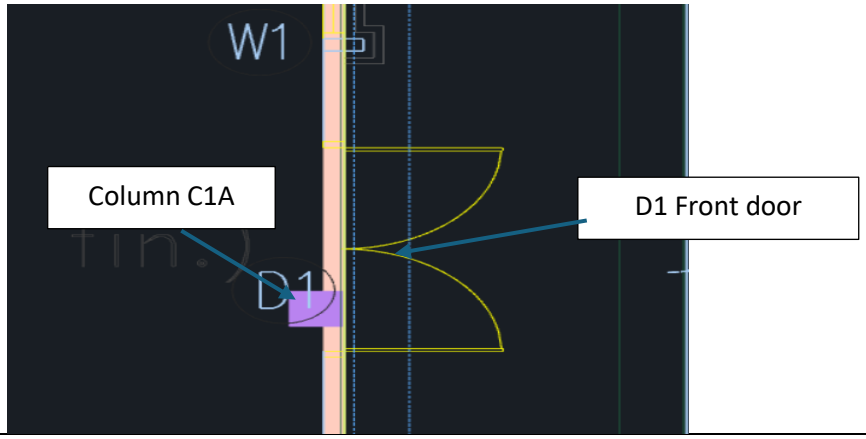
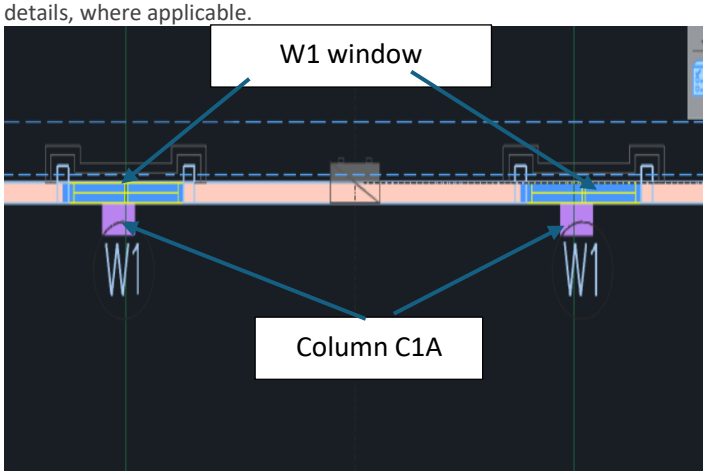
2-2-40, 2nd Floor Wisma Rampai,
Jalan 34/26, Taman Sri Rampai,
53300 Kuala Lumpur.

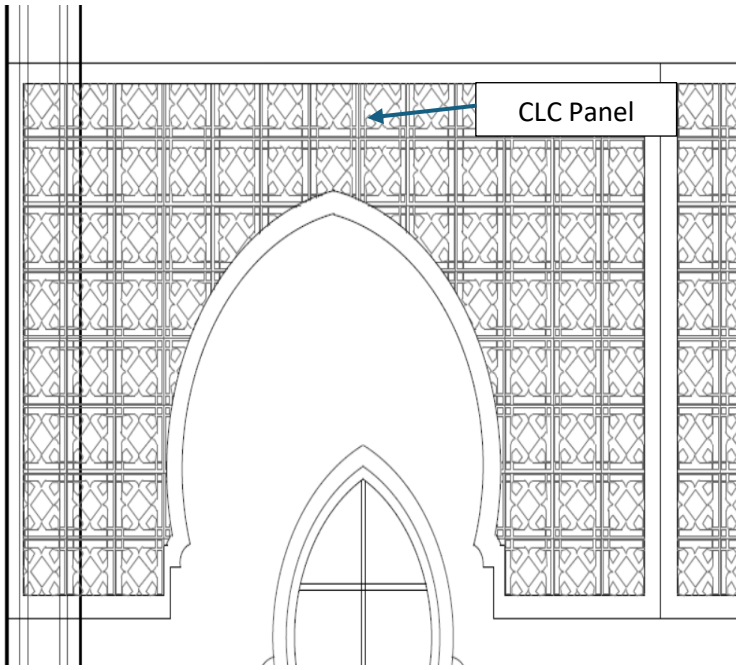
| | |
|---|---|
| No. Ruj / Ref No. | : ABM/KCG/N/T/QUE-01 |
| Tarikh / Date | : 24/8/2026 |
| Project Reference | PEMBANGUNAN YANG TERBINA "AS-BUILT"<br>BAGI CADANGAN PERUSAHAAN KOPI CAP GANTANG YANG<br>MENGANDUNGI :-<br>A. 1 UNIT BANGUNAN GUDANG (SEDIA ADA) - 1 TINGKAT<br>B. 1 UNIT BANGUNAN KILANG (ROBOH DAN BINA SEMULA) - 1 TINGKAT<br>C. 1 UNIT BANGUNAN PEJABAT (BAHARU) - 2 TINGKAT<br>D. 1 UNIT TAPAK KOMERSIAL (ROBOH DAN BINA SEMULA) - 1 TINGKAT<br>DI ATAS LOT 70125, 70126, 13004 & 13504, MUKIM PULAI,<br>DAERAH BALING, KEDAH DARUL AMAN.<br>GANTANG COFFEE ENTERPRISE SDN. BHD. (986590-K)<br>(PRODUK : MEMPROSES KOPI) |
| Perhatian / Attention | : THW CONSULTANTS SDN BHD |
| No. Tel. / Tel. No. | : 04-397 3779 |
| Email | : admin@thwsb.com |

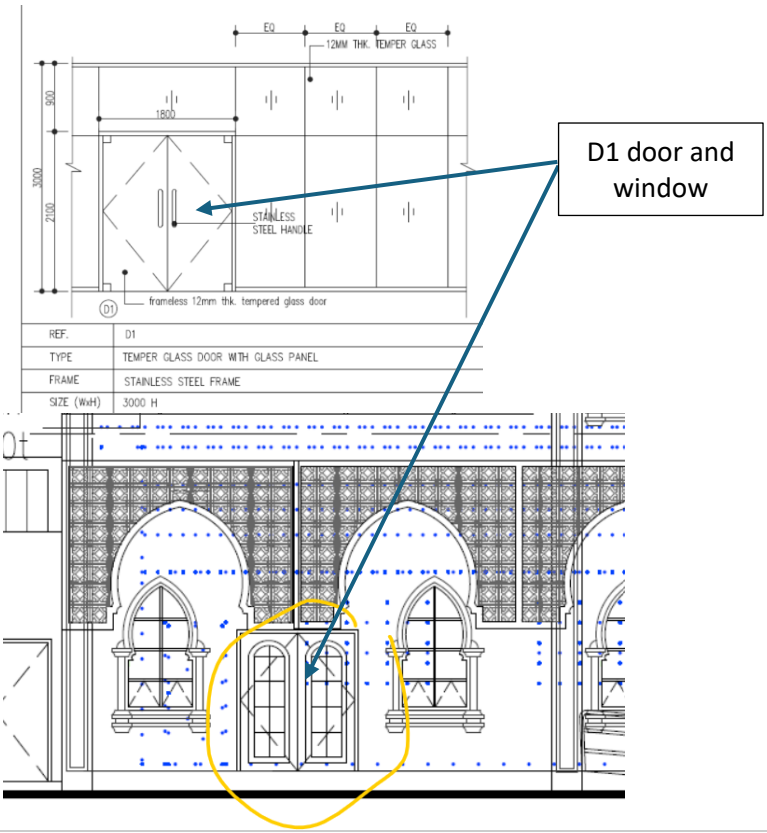
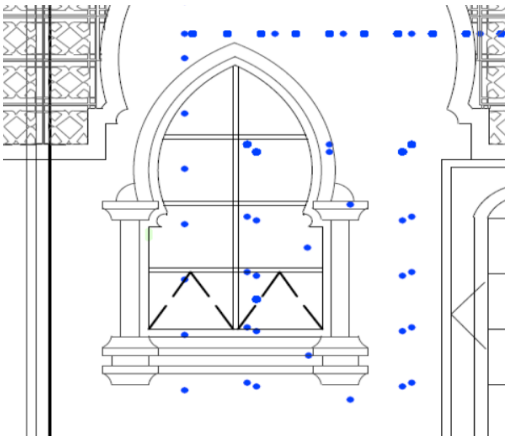
## QUERY LIST NO. 1

We would like to highlight the following queries for your review and further clarification:

| NO. | QUESTIONS / QUERY | REPLY/CLARIFICATIONS |
|---|---|---|
| | **Structural Works** | |
| 1 | **Demolition Works:** Please provide details and extent of the demolition works, including identification of the affected existing buildings/structures. Kindly confirm whether the existing old factory/kilang is to be demolished and whether the existing garage, guard house/pondok/TNB box, old surau and canteen are to remain.<br>  | |
| 2 | **Existing Concrete Accessway:** Please confirm whether the existing concrete accessway is to remain as-is or whether resurfacing, repair and/or making good works are required. | |
| 3 | **UB Tie Level: Please** confirm the required level/elevation of the UB tie & 100x100x4mm SHS. Kindly provide the relevant structural detail or section for reference.<br>  | |

| | | |
|---|---|---|
| 4 | **Brickwall Height:** Please confirm whether the brickwall height is 3,000mm measured from FFL. (Location : External Wall Kilang) | |
| 5 | **Existing Pile Extension:** Kindly provide the location plan identifying the existing piles that are required to be extended, as referenced in Drawing No. THWB/GCE/8308/RC3.<br>  <br> | |
| 6 | **Internal Warehouse Brickwall:** Please confirm the required height of the internal brickwalls within the warehouse, particularly for the Production Area, Packaging Area and Raw Material Area. | |
| 7 | **Column C1A Clash with Door D1**: There appears to be a clash between Column C1A and Door D1. Kindly review and confirm the intended arrangement / provide the revised architectural or structural detail.<br>  <br> | |
| 8 | **Column Clash with Window W1:** There appears to be a clash between certain columns and Window W1. Kindly review and confirm the intended arrangement and provide the revised details, where applicable.<br>  <br> | |

| | | |
|---|---|---|
| 9 | **Piling Works** : Please confirm the method of piling by hammer or injection piling? | |
| | **Architectural** | |
| 1 | **Gypsum Board Door with Glass Panel:** Please confirm the required door height, ceiling height, and size/dimensions of the glass panel. Kindly provide the relevant details/drawing for our pricing<br>(Location : Packaging Area, Bilik Bahan Mentah) | |
| 2 | **Flat Floor / Power Float Finish:** Please confirm whether a super-flat floor finish is required. If so, kindly confirm the required flatness specification / SR classification. Otherwise, please confirm whether a standard power-float / ride-on power-float finish is sufficient for the floor.<br>(Location : Flat floor slab at kilang) | |
| 3 | **Apron to Warehouse and Office**: Please confirm whether a concrete apron is required around the perimeter of the warehouse and office buildings. Kindly provide the extent, width and specification of the apron, if applicable. | |
| 4 | **Toilet Adjacent to Warehouse**: Please confirm whether the toilet partition is to be constructed using proprietary toilet cubicle partitions, as the door schedule indicates Door D11 with cubicle-type door material, or whether brickwall construction is required. Kindly confirm the intended wall and door arrangement. | |
| 5 | **Façade – CLC Wall Panel**: Please provide the detailed design/specification and construction details for the proposed CLC wall panel façade, including thickness, finish and fixing/support details. Kindly provide cut section.<br><br>(Location : External Façade perimeter of office)<br><br>  | |

| | | |
|---|---|---|
| 6 | **Discrepancy – Tempered Glass:** There appears to be a discrepancy between the Door & Window Schedule, which indicates tempered glass and window glass to D1, compared to the elevation drawing, which does not indicate tempered glass and shows a decorative panel door. Kindly confirm the correct requirement.<br>  | |
| 7 | **Internal Warehouse Walls:** Please confirm the required height of the internal walls within the warehouse. In particular, if the external wall height is 3,000mm but the internal shutter door height is 4,000mm, kindly confirm whether the internal wall is required to extend to the full ceiling/roof level or to a specific height | |
| 8 | **Window Coping / Window W1:** Please confirm whether lightweight/custom-made coping is acceptable for the window copings. Kindly also provide the detailed dimensions and construction details for coping of window W1.<br>  | |

AB MALAYA SDN BHD
(1601411-W)

2-2-40, 2nd Floor Wisma Rampai,
Jalan 34/26, Taman Sri Rampai,
53300 Kuala Lumpur.

| | | |
|---|---|---|
| 9 | **Office Ceiling Height:** Please confirm the finished ceiling height for the office areas at both Ground Floor and First Floor, where plasterboard ceiling is proposed. | |
| 10 | **Door & Window Schedule:** Door D9 details appear to be missing, and certain windows also appear to be without corresponding details. Kindly provide the latest updated Door & Window Schedule, including all missing door/window types, dimensions, materials and relevant details. | |

We trust the above queries are clear and would appreciate your clarification and confirmation on the respective items to enable us to proceed with our tender pricing accordingly.

Kindly revert with your clarification by Thursday, 27 August 2026, to allow us sufficient time to review and incorporate the necessary requirements into our tender submission.

Thank you.

Yours faithfully,

*AB MALAYA SDN. BHD.*

NURUL FALDZLYANA LAILY BINTI NOR SANY
